CONCEPTUAL SCHEDULE
SCENARIO 1: 2017/SMA-24 MODIFICATION
Stage 3 Waiau Proposal
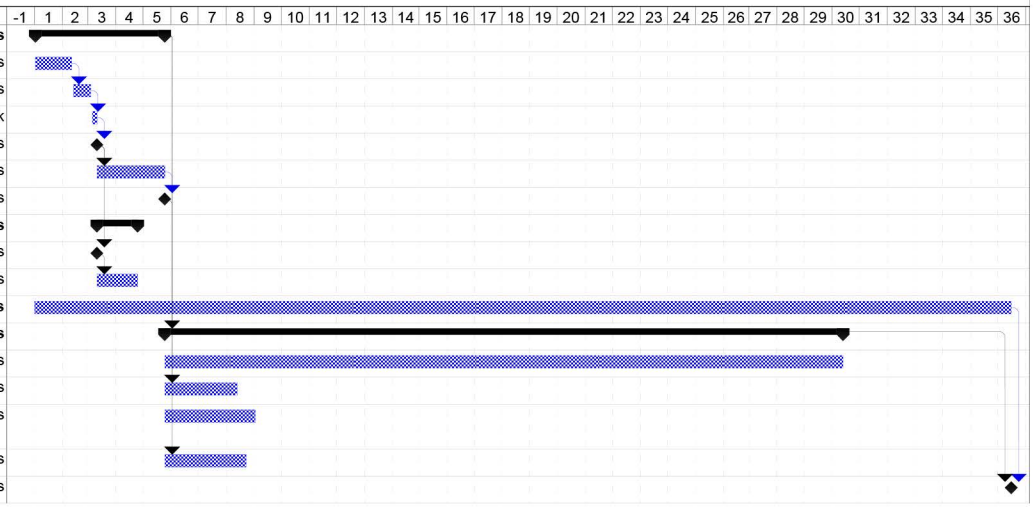
ID	Task Name	Duration
1	**Modification of 2017/SMA-24**	**103 days**
2	PSI prepares application	30 days
3	Client review	3 wks
4	PSI revise	1 wk
5	Sign and Submit Complete Applicatio	0 days
6	DPP-LUPD process	75 edays
7	Receive approval	0 days
8	**Historic Review (HRS Chapter 6E-42)**	**31 days**
9	Submit materials to SHPD	0 days
10	SHPD review	45 edays
11	**Air Permit Modification**	**36 emons**
12	**Other permits**	**536 days**
13	Modify NPDES permit	25 emons
14	CUP Minor Modification	80 edays
15	Noise Variance (if work is needed outside of normal work hours)	100 edays
16	Stockpiling and/or grading	90 edays
17	**Ground Breaking**	0 days
